



SE ISSAQUAH-FALL CITY ROAD PROJECT UPDATE




PROJECT COUNCIL BRIEFING 2

MAY 24, 2016


▶ PROJECT SCOPE & UPDATE

- ▶ Improve SE Issaquah-Fall City Road to the city's principal arterial standard between 247th PL SE and Klahanie Drive SE
- ▶ Project at 5% completion, recent work items include:
 - ☑ Interviews/meetings with schools, churches, local HOA's (~10)
 - ☑ Topographic Survey is underway
 - ☑ Project utilizing current traffic counts
 - ☑ Alternative analysis being done
 - ☑ Stream analysis underway
 - ☑ Public Meeting # 1, May 12

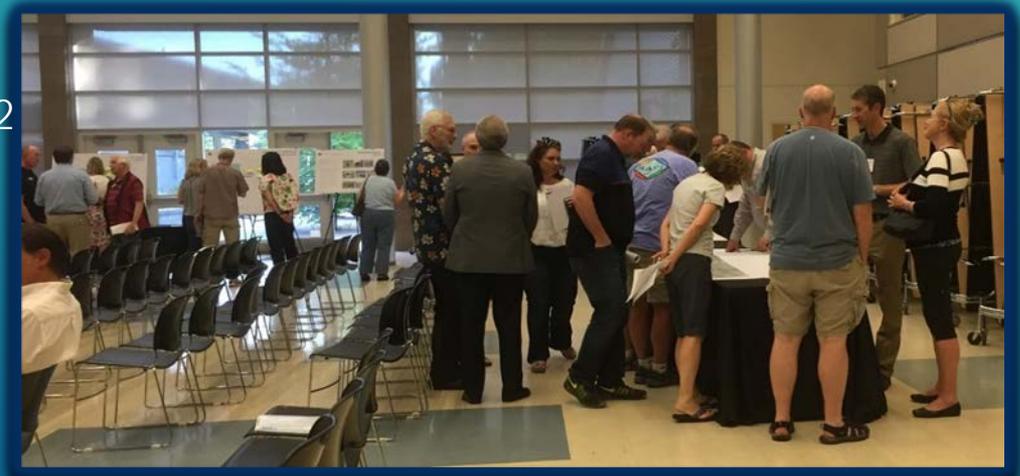

COMMUNITY WORKSHOP #1 SUMMARY, MAY 12, 2016

- ▶ Share project purpose, timeline and preliminary concepts
- ▶ Meeting included Project Presentation, Q&A, and an open house
- ▶ Attendees visited stations around the room
- ▶ Workshop attendees were asked to provide feedback
 - ▶ Preliminary roadway concepts
 - ▶ Intersection design options
 - ▶ North Fork Issaquah Creek crossing

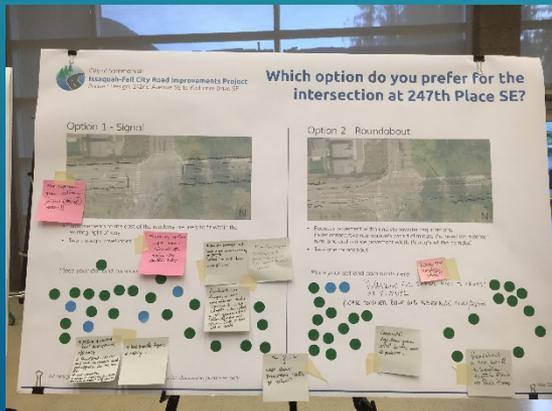


PUBLIC COMMENT...

Preferred concepts:

- ▶ 5-lane roadway with a buffered or protected bike lane throughout the corridor.
- ▶ Sidewalks and protected bike lanes on one or both sides.
- ▶ No clear preference for roundabouts or traffic signals. Use design option that keeps traffic moving.
- ▶ Concern for pedestrian and child safety along the corridor, specifically at the 247th Pl. SE intersection, middle school crossing.
- ▶ Interest in protecting green space and keeping existing trails where possible.

Next steps for the design team include:

- ▶ Update traffic model with intersection options
- ▶ Selection of Preferred Alternative for Phase 1
- ▶ Schedule Public Meeting # 2

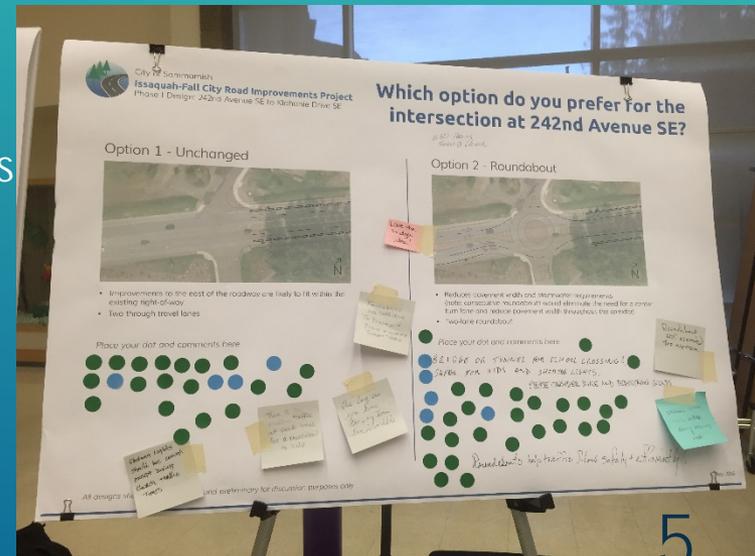

PROJECT SCHEDULE

▶ Upcoming Dates

- ▶ ~~April 19~~ ~~Council Brief 1~~
- ▶ ~~May 12~~ ~~Public Meeting 1, Pacific Cascade MS, 6-8pm~~
- ▶ May 24 Council Brief 2
- ▶ June-July Preferred Alternatives Presented to Trans Comm
- ▶ Early July Public Meeting 2, date TBD
- ▶ TBD Council Brief 3 – Alternative Selection
- ▶ *Sept* 30% Design Completion
- ▶ *Sept* Council Brief 4
- ▶ *Oct* Public Meeting 3
- ▶ *Nov* 60% Design Completion
- ▶ *Dec* Council Briefing 5
- ▶ *Feb 2017* 90 % Design Completion
- ▶ *March 2017* Public Meeting 4
