19-Jun-18

Zackuse Creek Fish Passage and Stream Restoration

Activity ID	Activity Name	Original Duration	Total Float	Start	Finish
Zackuse Creek Fish Passage and Stream Restoration Project		63	1	09-Jul-18	04-Oct-18
General Conditions		63	1	09-Jul-18	04-Oct-18
A1000	Notice to Proceed (NTP)	0	64	09-Jul-18	
A1110	Project Start	0	1	09-Jul-18	
A1090	Interim Milestone - Schedule A1 Completion	0	4		24-Sep-18*
A1100	Substantial Completion	0	1		04-Oct-18*
Schedule A1 - Stream Restoration		55	4	09-Jul-18	24-Sep-18
A1010	Mobilization	5	1	09-Jul-18	13-Jul-18
A1030	Locates	1	5	09-Jul-18	09-Jul-18
A1120	Temporary Power Drop (PSE)	1	5	09-Jul-18	09-Jul-18
A1020	Implement TESC	5	1	16-Jul-18	20-Jul-18
A1040	Tree Protection Measures	2	1	17-Jul-18	18-Jul-18
A1070	Clearing and Tree Removal	5	4	30-Jul-18	03-Aug-18
A1080	Temporary Access Road	5	4	06-Aug-18	10-Aug-18
A1130	Zackuse Creek New Alignment - Stream Channel Grading	15	4	13-Aug-18	31-Aug-18
A1140	Zackuse Creek New Alignment - Stream Improvements	15	4	04-Sep-18	24-Sep-18
Schedule A2 - ELSP Culvert Replacement		23	33	19-Jul-18	20-Aug-18
A1050	Sawcut	2	1	19-Jul-18	20-Jul-18
A1060	Install Dewatering System	5	1	23-Jul-18	27-Jul-18
A1260	Fish Exclusion and Fish Removal - Stage 1	3	2	23-Jul-18	25-Jul-18
A1250	Install Temp Bypass (in dewatering trench)	2	2	26-Jul-18	27-Jul-18
A1160	Existing Utility Re-Locates	4	2	30-Jul-18	02-Aug-18
A1150	E. Lake Sammamish Pkwy Closure	0	1	06-Aug-18	
A1190	Box Culvert Installation	8	1	06-Aug-18	15-Aug-18
A1290	Existing Watermain Shutdown	1	7	06-Aug-18	06-Aug-18
A1270	Fish Exclusion and Fish Removal - Stage 2	2	2	14-Aug-18	15-Aug-18
A1280	Release Zackuse Into New Alignment	0	36		15-Aug-18
A1310	PSE Gas - New Alignment	1	1	16-Aug-18	16-Aug-18
A1170	Restoration	2	1	17-Aug-18	20-Aug-18
A1300	E. Lake Sammamish Pkwy Re-Open	0	1		20-Aug-18
Schedule A3 - Water and Sewer - Final Configuration		32	1	21-Aug-18	04-Oct-18
A1220	Temporary Bypass - Stage 2	3	1	21-Aug-18	23-Aug-18
A1200	Sanitary Sewer Installation	5	1	24-Aug-18	30-Aug-18
A1210	Watermain Installation	4	1	31-Aug-18	06-Sep-18
A1230	Testing and Inspection	5	1	07-Sep-18	13-Sep-18
A1240	Restoration	10	1	14-Sep-18	27-Sep-18
A1320	Punchlist/Cleanup	5	1	28-Sep-18	04-Oct-18

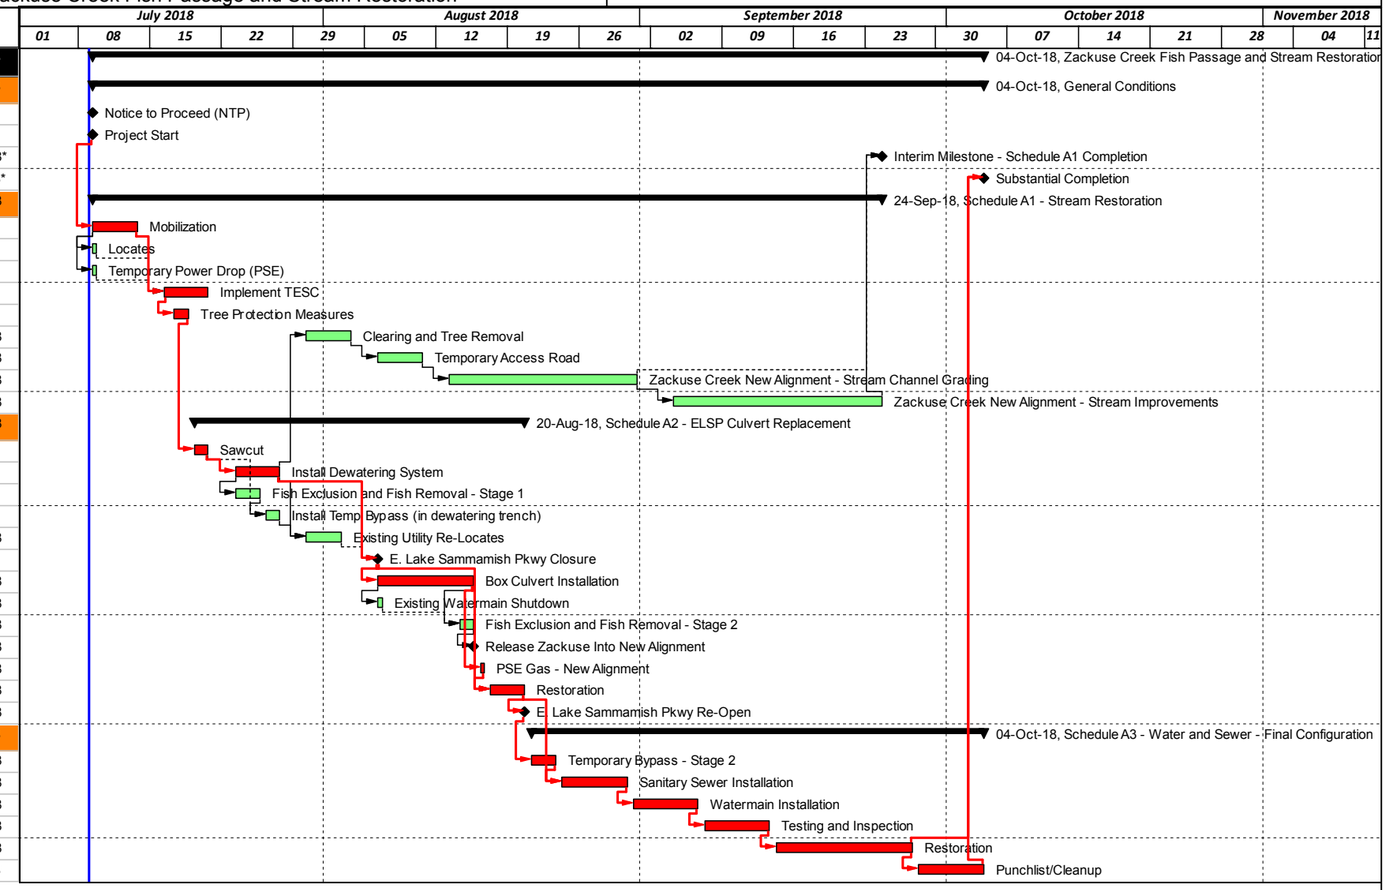

Total Closure Time

Remaining Level of Effort | Actual Work | Critical Remaining Work | Summary
Actual Level of Effort | Remaining Work | Milestone

Pacifc Civil & Infrastructure - Baseline Schedule
